

PERMASNAP DUAL CANTILEVER WELDED RADIUS COPING

IMPORTANT!!! MUST INDICATE PROPER RADIUS CONDITION BY CIRCLING APPROPRIATE OUTSIDE FACE

PROVIDING A RADIUS
THE RADIUS MAY BE PROVIDED
IN ONE OF TWO METHODS:

1.) THE ACTUAL KNOWN RADIUS IS


_____ ' FEET _____ " INCHES MINIMUM OF 3'-0"

OR

2.) FIELD CONDITION MEASUREMENTS

NOTE: REFER TO ATTACHED WORKSHEET FOR FURTHER INFORMATION

_____ " INCHES

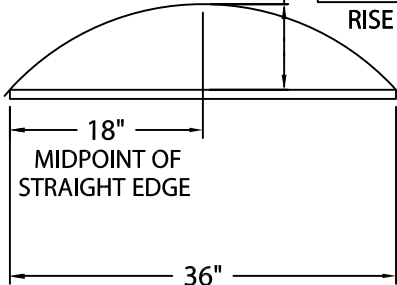


36" LENGTH OF STRAIGHT EDGE
NOTE: CHECK MEASUREMENTS ALONG ENTIRE RADIUS.
DETAIL A

RISE MAXIMUM OF 4 3/4"

OUTSIDE FACE OUTSIDE FACE

ROOF LINE RADIUS (PROVIDED BY APPROVER PER DETAIL A)

TOP VIEW

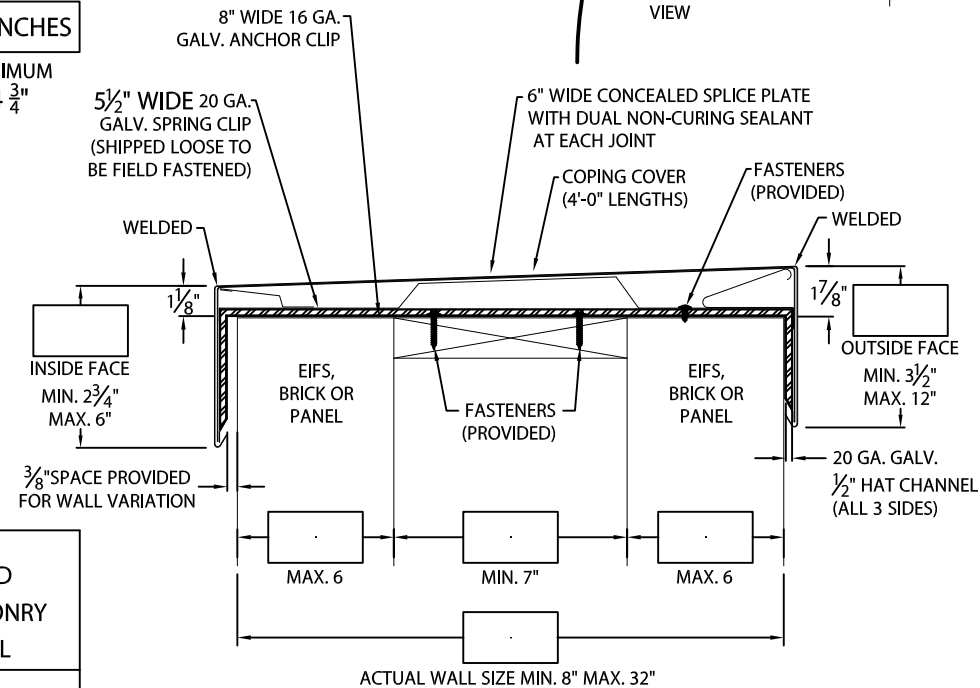

PLEASE SPECIFY SUBSTRATE: (IF SUBSTRATE INFORMATION IS NOT GIVEN, WOOD SUBSTRATE FASTENERS WILL BE PROVIDED)

WOOD MASONRY METAL

NOTES:
-- Concealed splice plates are provided with factory applied dual non-curing sealants.

Fabrication will proceed only after receipt of signed print approval.

Print Approval:
Architect and/or contractor shall verify all dimensions, sizes and quantities. All products to be installed in strict accordance with printed instructions.

Approved by: _____
Date: _____

MATERIALS:
TOP - .080" ALUM.
SIDES - .063" ALUM.
COLOR: _____
FINISH: _____

QUANTITIES:
_____ LINEAL FEET 4'-0" LENGTHS

PROJECT: _____
ARCHITECT: _____
ROOFING CONTRACTOR: _____
REPRESENTATIVE/DISTRIBUTOR: _____

Hickman Edge Systems
4 Commerce Way
Arden, NC 28704
Phone: 828-676-1700
www.hickmanedgesystems.com



DATE: 08/04/23 SHT.# _____ OF _____
DRN BY: MLM
CKD BY: MM DWG# 64011-39301 **B**
