


CREATIVE DESIGN LEAK-TITE COPING

TAPERED VERSION

ANSI/SPRI ES-1 TESTED

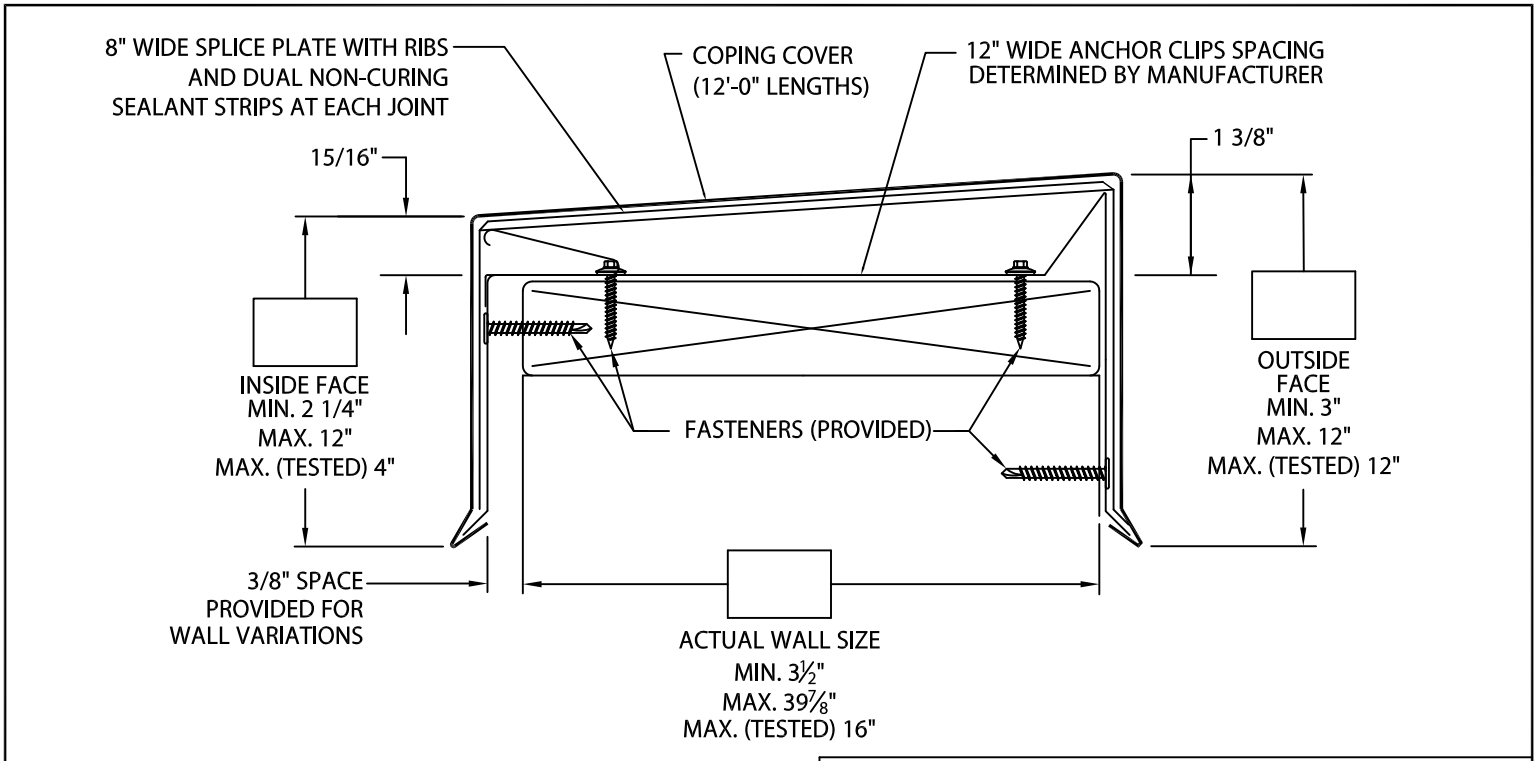

PLEASE SPECIFY SUBSTRATE: (IF SUBSTRATE INFORMATION IS NOT GIVEN, WOOD SUBSTRATE FASTENERS WILL BE PROVIDED)

WOOD
 MASONRY
 METAL

-- CONCEALED SPLICE PLATES ARE PROVIDED WITH FACTORY APPLIED DUAL NON-CURING SEALANT STRIPS.
 -- UNLESS OTHERWISE NOTED, FABRICATION OF MITERS AND ACCESSORIES ARE FURNISHED STANDARD UTILIZING A NON-PENETRATING QUICKLOCK JOINT, THEN FACTORY SEALED WATERTIGHT.

-- WELDED MITERS AND ACCESSORIES
 CHECK ONE REQUIRED (SURCHARGE) NOT APPLICABLE

Fabrication will proceed only after receipt of signed print approval.

Print Approval:

Architect and/or contractor shall verify all dimensions, sizes and quantities. All products to be installed in strict accordance with printed instructions.

Approved by: _____

Date: _____

MATERIAL:

__ 24 GA. GALV. __ .050" ALUMINUM
 __ 22 GA. GALV. __ .063" ALUMINUM
 __ .040" ALUMINUM
 __ OTHER _____

COLOR: _____ FINISH: _____

QUANTITIES:

_____ LINEAL FEET 12'-0" LENGTHS
 _____ OUTSIDE MITERS @ (_____)°
 _____ INSIDE MITERS @ (_____)°
 _____ RIGHT END CAPS
 _____ LEFT END CAPS

PROJECT: _____
 ARCHITECT: _____
 ROOFING CONTRACTOR: _____
 REPRESENTATIVE/DISTRIBUTOR: _____

Hickman Edge Systems
 4 Commerce Way
 Arden, NC 28704
 Phone: 828-676-1700
 www.hickmanedgesystems.com

HICKMAN
 an MTL company

DATE: 06/20/23 SHT.# _____ OF _____
 DRN BY: MLM
 CKD BY: MM DWG# 64011-36839 **B**
