


## PERMASPAN RW EXPANSION JOINT ROOF TO WALL

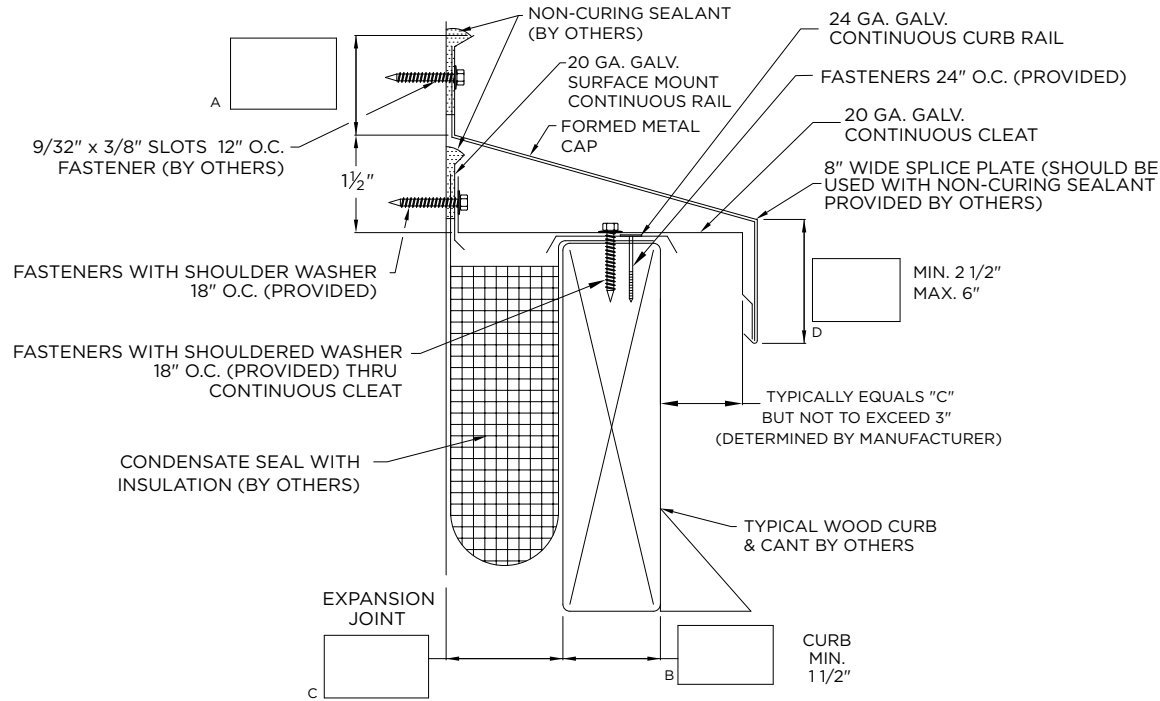

### NOTES

- Unless otherwise noted, fabrication of miters and accessories are furnished standard utilizing a non-penetrating quicklock joint, then factory sealed watertight
- Welded accessories require a minimum material thickness of .050"
- For non-90 miters, see separate print approval
- Product should be installed per provided installation instructions

### PROJECT INFO

Project Name: \_\_\_\_\_

Architect: \_\_\_\_\_

Roofing Contractor: \_\_\_\_\_

#### Project Type:

By selecting this box you have verified and confirmed that dimensions, sizes, and quantities are correct. All products will be installed in strict accordance with printed instructions.

SHT# 1 of 1  
DATE: 02/07/22

Date: \_\_\_\_\_

#### Hickman Edge Systems

4 Commerce Way  
Arden, NC 28704  
Phone: 828-676-1700  
www.hickmanedgesystems.com

DRN BY: JJC  
CKD BY: MM  
DWG #: 64028-37154  
REV: A

### DIMENSIONS

PLEASE FILL OUT DIMENSIONS ON DRAWING

### MATERIAL

- 24 Ga. Galv. Steel
- 22 Ga. Galv. Steel
- .040" Aluminum
- .050" Aluminum
- .063" Aluminum
- OTHER: \_\_\_\_\_

Color: \_\_\_\_\_

Finish: \_\_\_\_\_

Substrate:

If substrate is not given, wood fasteners will be provided.

- Wood
- Masonry
- Metal

### QUANTITIES

\_\_\_\_\_ Lineal Feet (12'-0" Lengths)

\_\_\_\_\_ Outside Miters (90°)

\_\_\_\_\_ Inside Miters (90°)

\_\_\_\_\_ Right Endcap Inserts (As seen from roof)

\_\_\_\_\_ Left Endcap Inserts (As seen from roof)

\_\_\_\_\_ Right Endwall Flashings (As seen from roof)(.040" Mill Painted/Welded Only)

\_\_\_\_\_ Left Endwall Flashings (As seen from roof)(.040" Mill Painted/Welded Only)

Accessory Type:  Quicklock (Default)  Welded (Surcharge)
