



PERMASNAP CONTINUOUS CLEAT QUICKLOCK RADIUS COPING

TAPERED VERSION

TO BE USED WITH CONTINUOUS CLEAT COPING

IMPORTANT!!! MUST INDICATE PROPER RADIUS CONDITION BY CIRCLING APPROPRIATE OUTSIDE FACE

PROVIDING A RADIUS
THE RADIUS MAY BE PROVIDED
IN ONE OF TWO METHODS:


1.) THE ACTUAL KNOWN RADIUS IS

_____ ' FEET _____ " INCHES MINIMUM OF 3'-0"

OR



2.) FIELD CONDITION MEASUREMENTS

NOTE: REFER TO ATTACHED WORKSHEET
FOR FURTHER INFORMATION

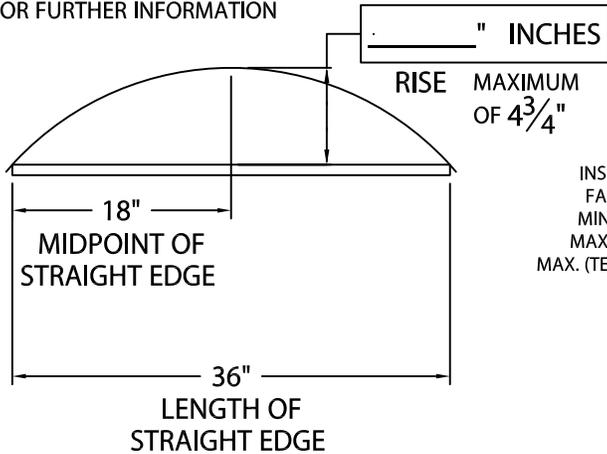

NOTE: CHECK MEASUREMENTS ALONG ENTIRE RADIUS.

DETAIL A

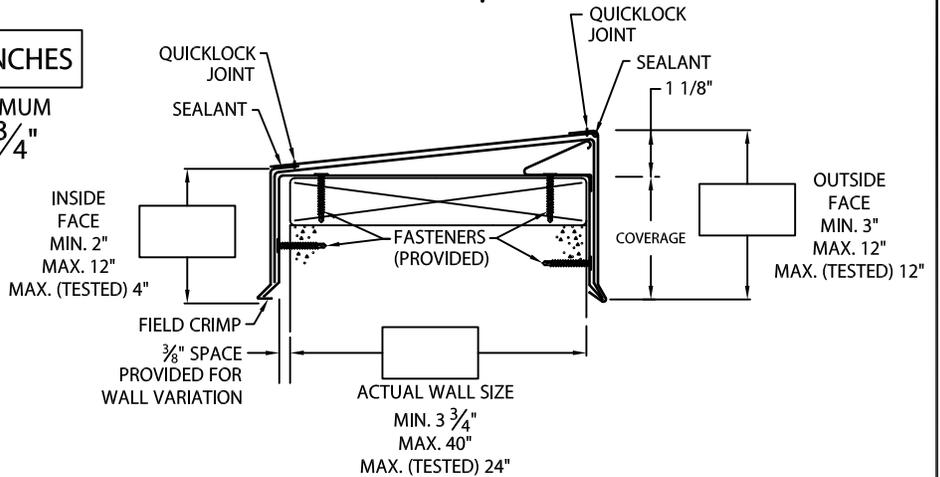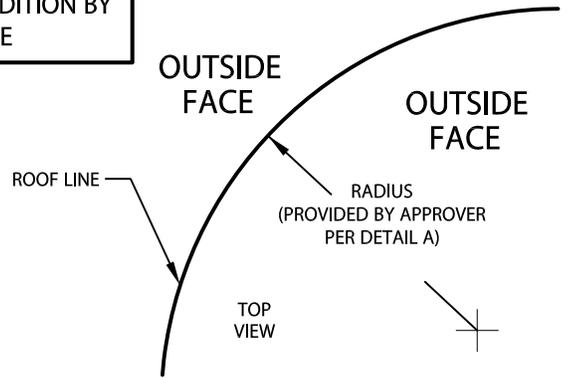

PLEASE SPECIFY SUBSTRATE:
(IF SUBSTRATE INFORMATION IS NOT GIVEN, WOOD SUBSTRATE FASTENERS WILL BE PROVIDED)

WOOD
 MASONRY
 METAL

NOTES: -- CONCEALED SPLICE PLATES ARE PROVIDED WITH FACTORY APPLIED DUAL NON-CURING SEALANT STRIPS.
-- FABRICATION OF RADIUS IS FURNISHED UTILIZING NON-PENETRATING QUICKLOCK JOINT, THEN FACTORY SEALED WATERTIGHT

MATERIAL:

___ 24 GA. GALVANIZED STEEL ___ .050" ALUMINUM
___ 22 GA. GALVANIZED STEEL ___ .063" ALUMINUM
___ .040" ALUMINUM ___ OTHER _____

COLOR: _____ FINISH: _____

QUANTITIES:

_____ LINEAL FEET 4'-0" LENGTHS

Fabrication will proceed only after receipt of signed print approval.

Print Approval:

Architect and/or contractor shall verify all dimensions, sizes and quantities. All products to be installed in strict accordance with printed instructions.

Approved by: _____

Date: _____

PROJECT:

ARCHITECT:

ROOFING CONTRACTOR:

REPRESENTATIVE/DISTRIBUTOR:

Hickman Edge Systems

4 Commerce Way

Arden, NC 28704

Phone: 828-676-1700

www.hickmanedgesystems.com

DATE: 08/04/23

SHT.# ___ OF ___

DRN BY: MLM

CKD BY: MM

DWG# 64011-39285

